



ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	M	J
1			Notice to Proceed	0 days	Mon 9/15/25	Mon 9/15/25				
2			Man Hole Apprvoal	0 days	Tue 10/7/25	Tue 10/7/25				
3			Mobilize	2 days	Mon 10/13/25	Wed 10/15/25		Crew 1		
4			Office Trailer Prep Work	1 day	Wed 10/15/25	Thu 10/16/25	3	Crew 1		
5			Excavate Bore Pit 16+87	3 days	Thu 10/16/25	Thu 10/23/25	4	Crew 1		
6			Bore MH6-MH26	13 days	Thu 10/23/25	Thu 11/20/25	5	Sub		
7			Install MH9	2 days	Thu 10/23/25	Tue 10/28/25	5	Crew 1		
8			Install 8" Sewer MH9-MH10	2 days	Wed 10/29/25	Mon 11/3/25	7	Crew 1		
9			Telephone Pole Relocated	0 days	Mon 11/3/25	Mon 11/3/25	10			
10			Rail Road Approval Begin Road Closure	0 days	Mon 11/3/25	Mon 11/3/25				
11			Clearing and Grubbing	1 day	Mon 11/3/25	Tue 11/4/25	9	2 Crew		
12			Install MH10	1 day	Mon 11/3/25	Tue 11/4/25	8	Crew 1		
13			Excavate Bore Pit 0+25	3 days	Tue 11/4/25	Mon 11/10/25	11	2 Crew		
14			Bore 0+25-1+60	13 days	Tue 11/11/25	Wed 12/10/25	13	Sub		
15			Temporary Access	5 days	Tue 11/11/25	Thu 11/20/25	13	2 Crew		
16			Install 8" Sewer MH10-MH11	2 days	Tue 11/4/25	Mon 11/10/25	12	Crew 1		
17			Install MH11	2 days	Mon 11/10/25	Wed 11/12/25	16	Crew 1		
18			Install 8" Sewer MH11-MH12	3 days	Wed 11/12/25	Wed 11/19/25	17	Crew 1		
19			Clearing and Grubbing	3 days	Thu 11/20/25	Wed 11/26/25	15	2 Crew		
20			Install MH12	2 days	Wed 11/19/25	Mon 11/24/25	18	Crew 1		
21			Excavate Receiving Pit MH 26	2 days	Mon 12/1/25	Wed 12/3/25	19	2 Crew		
22			Install 8" Sewer MH12-MH13	2 days	Tue 11/25/25	Mon 12/1/25	20	Crew 1		
23			Excavate Receiving Pit 1+60	2 days	Wed 12/3/25	Mon 12/8/25	21	2 Crew		
24			Install MH13	2 days	Mon 12/1/25	Wed 12/3/25	22	Crew 1		
25			Install 8" Sewer MH13-MH14	1 day	Thu 12/4/25	Mon 12/8/25	24	Crew 1		
Project: Construction Schedule Pr Date: Wed 10/1/25			Task		Inactive Task		Start-only			
			Split		Inactive Milestone		Finish-only			
			Milestone		Inactive Summary		Deadline			
			Summary		Manual Task		Progress			
			Project Summary		Duration-only		Manual Progress			
			External Tasks		Manual Summary Rollup					
			External Milestone		Manual Summary					
Page 1										

SUBJECT TO CHANGE

ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	M	J
26			Install MH14	2 days	Mon 12/8/25	Wed 12/10/25	25	Crew 1		
27			Install MH26	3 days	Tue 12/9/25	Mon 12/15/25	23	2 Crew		
28			Clearing and Grubbing	4 days	Mon 12/15/25	Tue 12/23/25	27	2 Crew		
29			Install 8" Sewer MH14-15	3 days	Wed 12/10/25	Wed 12/17/25	26	Crew 1		
30			Directional Drill 8" 1+60-8+60	11 days	Wed 12/17/25	Thu 1/15/26	14	Sub		
31			Install MH15	2 days	Wed 12/17/25	Mon 12/22/25	29	Crew 1		
32			Install MH6	2 days	Tue 12/23/25	Mon 1/5/26	28	2 Crew		
33			Install 8" Sewer MH15-MH16	4 days	Tue 12/23/25	Tue 1/6/26	31	Crew 1		
34			Install 8" Sewer MH6-MH7	2 days	Mon 1/5/26	Wed 1/7/26	32	2 Crew		
35			Install MH 7	1 day	Wed 1/7/26	Thu 1/8/26	34	2 Crew		
36			Install 8" sewer MH7-MH8	2 days	Mon 1/12/26	Wed 1/14/26	35	2 Crew		
37			Install MH16	2 days	Wed 1/7/26	Mon 1/12/26	33	Crew 1		
38			Install MH8	1 day	Wed 1/14/26	Thu 1/15/26	36	2 Crew		
39			Install 8" Sewer MH16-MH17	2 days	Mon 1/12/26	Wed 1/14/26	37	Crew 1		
40			Install 8" MH8-MH9	2 days	Thu 1/15/26	Wed 1/21/26	38	2 Crew		
41			Install MH17	2 days	Thu 1/15/26	Tue 1/20/26	39	Crew 1		
42			Install Laterals Cabana Club Driveway	3 days	Wed 1/21/26	Tue 1/27/26	40	2 Crew		
43			Directional Drill 8" 8+60-16+20	14 days	Thu 1/15/26	Tue 2/17/26	30	Sub		
44			Install 8" Sewer MH26-MH27	5 days	Wed 1/28/26	Mon 2/9/26	42	2 Crew		
45			Install 8" Sewer MH17-MH18	6 days	Tue 1/20/26	Mon 2/2/26	41	Crew 1		
46			Install MH27	3 days	Mon 2/9/26	Thu 2/12/26	44	2 Crew		
47			Install MH 18	3 days	Tue 2/3/26	Mon 2/9/26	45	Crew 1		
48			Install Sewer Laterals MH26-MH27	6 days	Mon 2/16/26	Thu 2/26/26	46	2 Crew		
49			Install 8" Sewer MH18-MH19	7 days	Mon 2/9/26	Tue 2/24/26	47	Crew 1		
50			Install MH 1 Connect to Stub 0+00	3 days	Thu 2/26/26	Thu 3/5/26	48	2 Crew		

Project: Construction Schedule Pr
Date: Wed 10/1/25

Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Progress	
Project Summary		Duration-only		Manual Progress	
External Tasks		Manual Summary Rollup			
External Milestone		Manual Summary			

ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	M	J
51			Install MH19	2 days	Tue 2/24/26	Thu 2/26/26	49	Crew 1		
52			Install MH 2	4 days	Thu 3/5/26	Mon 3/16/26	50	2 Crew		
53			Install MH19-MH20	2 days	Mon 3/2/26	Wed 3/4/26	51	Crew 1		
54			Restore Camargo	2 days	Mon 3/16/26	Wed 3/18/26	52	2 Crew		
55			Install MH20	2 days	Wed 3/4/26	Mon 3/9/26	53	Crew 1		
56			Install 8" Sewer MH20-MH21	2 days	Tue 3/10/26	Thu 3/12/26	55	Crew 1		
57			Install MH 5	3 days	Wed 3/18/26	Wed 3/25/26	54	2 Crew		
58			Install MH21	2 days	Thu 3/12/26	Tue 3/17/26	56	Crew 1		
59			Install 8" Sewer MH5-MH6	3 days	Wed 3/25/26	Wed 4/1/26	57	2 Crew		
60			Install 8" Sewer MH21-MH22	4 days	Wed 3/18/26	Wed 3/25/26	58	Crew 1		
61			Install remaining laterals Cabana Club Driveway	2 days	Wed 4/1/26	Mon 4/6/26	59	2 Crew		
62			Grade and Prep Cabana Club for Paving	4 days	Mon 4/6/26	Tue 4/14/26	61	2 Crew		
63			Install MH22	2 days	Thu 3/26/26	Tue 3/31/26	60	Crew 1		
64			Install 8" Sewer MH22-MH23	4 days	Tue 3/31/26	Wed 4/8/26	63	Crew 1		
65			Pave Cabana Club Drive	3 days	Tue 4/14/26	Tue 4/21/26	62	2 Crew		
66			Install MH23	3 days	Wed 4/8/26	Wed 4/15/26	64	Crew 1		
67			Seed and Restore Cabana Club Drive	1 day	Tue 4/21/26	Wed 4/22/26	65	2 Crew		
68			Install MH4	5 days	Wed 4/22/26	Mon 5/4/26	67	2 Crew		
69			Install 8" Sewer and 2" Conduit MH23-MH24	5 days	Wed 4/15/26	Mon 4/27/26	66	Crew 1		
70			Install MH24	1 day	Mon 4/27/26	Tue 4/28/26	69	Crew 1		
71			Cabana Club Opening	0 days	Thu 4/30/26	Thu 4/30/26				
72			Install MH51	4 days	Tue 5/5/26	Tue 5/12/26	68	2 Crew		
73			Install 8" Sewer and 2" Conduit MH23-MH45	3 days	Tue 4/28/26	Tue 5/5/26	70	Crew 1		
74			Install MH 3	4 days	Wed 5/13/26	Wed 5/20/26	72	2 Crew		
75			Install MH45	2 days	Tue 5/5/26	Thu 5/7/26	73	Crew 1		

Project: Construction Schedule Pr
Date: Wed 10/1/25

Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Progress	
Project Summary		Duration-only		Manual Progress	
External Tasks		Manual Summary Rollup			
External Milestone		Manual Summary			

ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	M	J
76			Install 8" Sewer and 2" Conduit MH45-MH46	3 days	Mon 5/11/26	Thu 5/14/26	75	Crew 1		
77			Install MH46	1 day	Thu 5/14/26	Mon 5/18/26	76	Crew 1		
78			Install 8" Sewer MH23-MH48	5 days	Tue 5/19/26	Thu 5/28/26	77	Crew 1		
79			Restore Sta. 1+60-12+76	11 days	Thu 5/21/26	Mon 6/15/26	74	2 Crew		
80			Install MH48	2 days	Thu 5/28/26	Tue 6/2/26	78	Crew 1		
81			Install 8" Sewer MH48-MH49	2 days	Tue 6/2/26	Mon 6/8/26	80	Crew 1		
82			Install MH49	1 day	Mon 6/8/26	Tue 6/9/26	81	Crew 1		
83			Install 8" Sewer MH21-MH50	2 days	Tue 6/9/26	Thu 6/11/26	82	Crew 1		
84			Install MH50	1 day	Mon 6/15/26	Tue 6/16/26	83	Crew 1		
85			Install Sewer MH9-MH33	4 days	Tue 6/16/26	Wed 6/24/26	84	Crew 1		
86			Force Main Complete 46-47	5 days	Mon 6/15/26	Wed 6/24/26	79	2 Crew		
87			Force Main Complete MH24-MH25	8 days	Thu 6/25/26	Mon 7/13/26	86	2 Crew		
88			Force Main Complete MH50-MH44	4 days	Tue 7/14/26	Tue 7/21/26	87	2 Crew		
89			Install MH 33	2 days	Wed 6/24/26	Mon 6/29/26	85	Crew 1		
90			Install Sewer MH33-MH35	6 days	Mon 6/29/26	Mon 7/13/26	89	Crew 1		
91			Install MH35	2 days	Mon 7/13/26	Wed 7/15/26	90	Crew 1		
92			Install 8" Sewer MH19-MH43	4 days	Wed 7/22/26	Wed 7/29/26	88	2 Crew		
93			Install 8" Sewer MH35-MH36	6 days	Wed 7/15/26	Wed 7/29/26	91	Crew 1		
94			Install MH43	2 days	Thu 7/30/26	Tue 8/4/26	92	2 Crew		
95			Install Sewer Laterals MH19-MH43	3 days	Tue 8/4/26	Tue 8/11/26	94	2 Crew		
96			Install Sewer Laterals MH23-MH49	6 days	Tue 8/11/26	Mon 8/24/26	95	2 Crew		
97			Install MH36	2 days	Wed 7/29/26	Mon 8/3/26	93	Crew 1		
98			Install 8" Sewer MH36-MH37	5 days	Mon 8/3/26	Wed 8/12/26	97	Crew 1		
99			Install Sewer Laterals MH23-MH46	3 days	Mon 8/24/26	Mon 8/31/26	96	2 Crew		
100			Install MH37	2 days	Thu 8/13/26	Tue 8/18/26	98	Crew 1		

Project: Construction Schedule Pr
Date: Wed 10/1/25

Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Progress	
Project Summary		Duration-only		Manual Progress	
External Tasks		Manual Summary Rollup			
External Milestone		Manual Summary			


ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	M	J
101			Force Main Complete MH35-MH40	8 days	Mon 8/31/26	Wed 9/16/26	99	2 Crew		
102			Install 8" Sewer MH37-MH38	3 days	Tue 8/18/26	Tue 8/25/26	100	Crew 1		
103			Install MH38	2 days	Tue 8/25/26	Thu 8/27/26	102	Crew 1		
104			Install 8" Sewer MH38-MH39	2 days	Thu 8/27/26	Wed 9/2/26	103	Crew 1		
105			Install MH39	1 day	Wed 9/2/26	Thu 9/3/26	104	Crew 1		
106			Install Sewer Laterals MH19-MH24	8 days	Wed 9/16/26	Mon 10/5/26	101	2 Crew		
107			Install 8" Sewer and 2" Conduit MH37-MH41	4 days	Thu 9/3/26	Mon 9/14/26	105	Crew 1		
108			Install MH41	2 days	Mon 9/14/26	Wed 9/16/26	107	Crew 1		
109			Install 8" Sewer MH26-MH28	3 days	Thu 9/17/26	Wed 9/23/26	108	Crew 1		
110			Install Sewer Laterals MH9-19	19 days	Mon 10/5/26	Mon 11/16/26	106	2 Crew		
111			Install MH28	1 day	Wed 9/23/26	Thu 9/24/26	109	Crew 1		
112			Install 8" Sewer MH28-MH29	2 days	Mon 9/28/26	Wed 9/30/26	111	Crew 1		
113			Install MH29	2 days	Wed 9/30/26	Mon 10/5/26	112	Crew 1		
114			Install 8" Sewer MH29-MH30	3 days	Tue 10/6/26	Mon 10/12/26	113	Crew 1		
115			Install MH30	2 days	Mon 10/12/26	Thu 10/15/26	114	Crew 1		
116			Install 8" Sewer MH30-MH31	6 days	Thu 10/15/26	Wed 10/28/26	115	Crew 1		
117			Install MH31	3 days	Wed 10/28/26	Wed 11/4/26	116	Crew 1		
118			Force Main Complete MH42-MH41	4 days	Mon 11/16/26	Tue 11/24/26	110	2 Crew		
119			Install 8" Sewer MH31-MH32	5 days	Wed 11/4/26	Mon 11/16/26	117	Crew 1		
120			Intall Sewer Lateral MH21-MH50	2 days	Tue 11/24/26	Mon 11/30/26	118	2 Crew		
121			Install MH32	2 days	Mon 11/16/26	Thu 11/19/26	119	Crew 1		
122			Install Sewer Laterals MH37-MH41	2 days	Mon 11/30/26	Thu 12/3/26	120	2 Crew		
123			Install Sewer Laterals MH37-39	4 days	Thu 12/3/26	Mon 12/14/26	122	2 Crew		
124			Install Sewer Laterals MH37-MH9	9 days	Mon 12/14/26	Fri 1/8/27	123	2 Crew		
125			Install Sewer Laterals MH26-32	17 days	Thu 11/19/26	Wed 1/6/27	121	Crew 1		


Project: Construction Schedule Pr
Date: Wed 10/1/25

Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Progress	
Project Summary		Duration-only		Manual Progress	
External Tasks		Manual Summary Rollup			
External Milestone		Manual Summary			

ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	M	J
126			Substantial Completion 480 Days From NTP	0 days	Fri 1/8/27	Fri 1/8/27				
127			Concrete Restoration	20 days	Wed 1/6/27	Wed 2/17/27	125	Crew 1		
128			Sod Restoration	16 days	Wed 2/17/27	Wed 3/24/27	127	Crew 1		
129			Asphalt Grind and Pave	7 days	Wed 3/24/27	Thu 4/8/27	128			
130			Final Completion 90 Days from Substantial	0 days	Thu 4/8/27	Thu 4/8/27				


Project: Construction Schedule Pr Date: Wed 10/1/25	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Progress	
	Project Summary		Duration-only		Manual Progress	
	External Tasks		Manual Summary Rollup			
	External Milestone		Manual Summary			

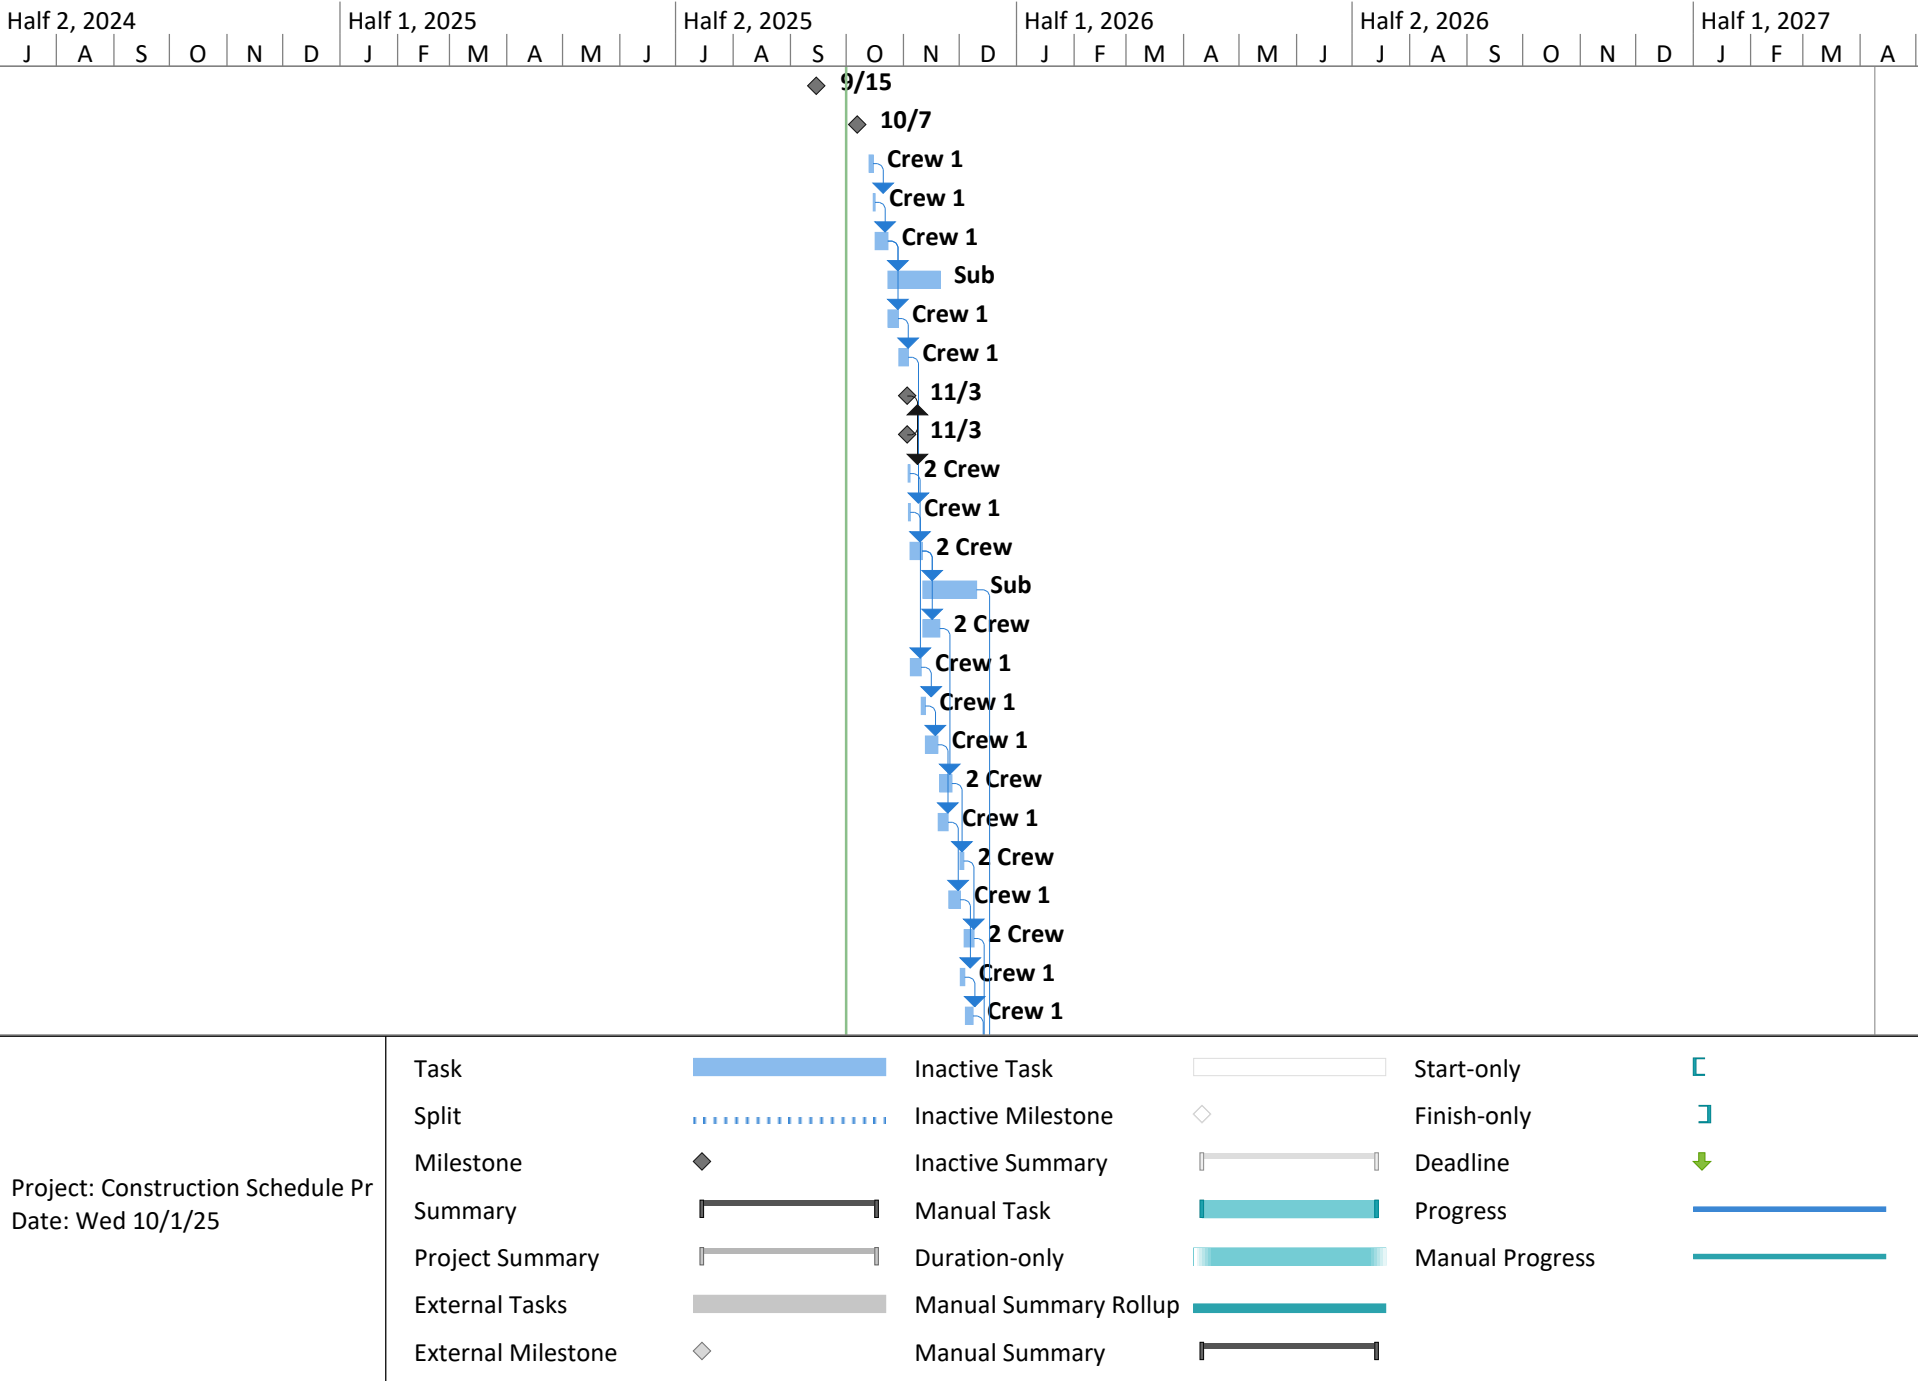

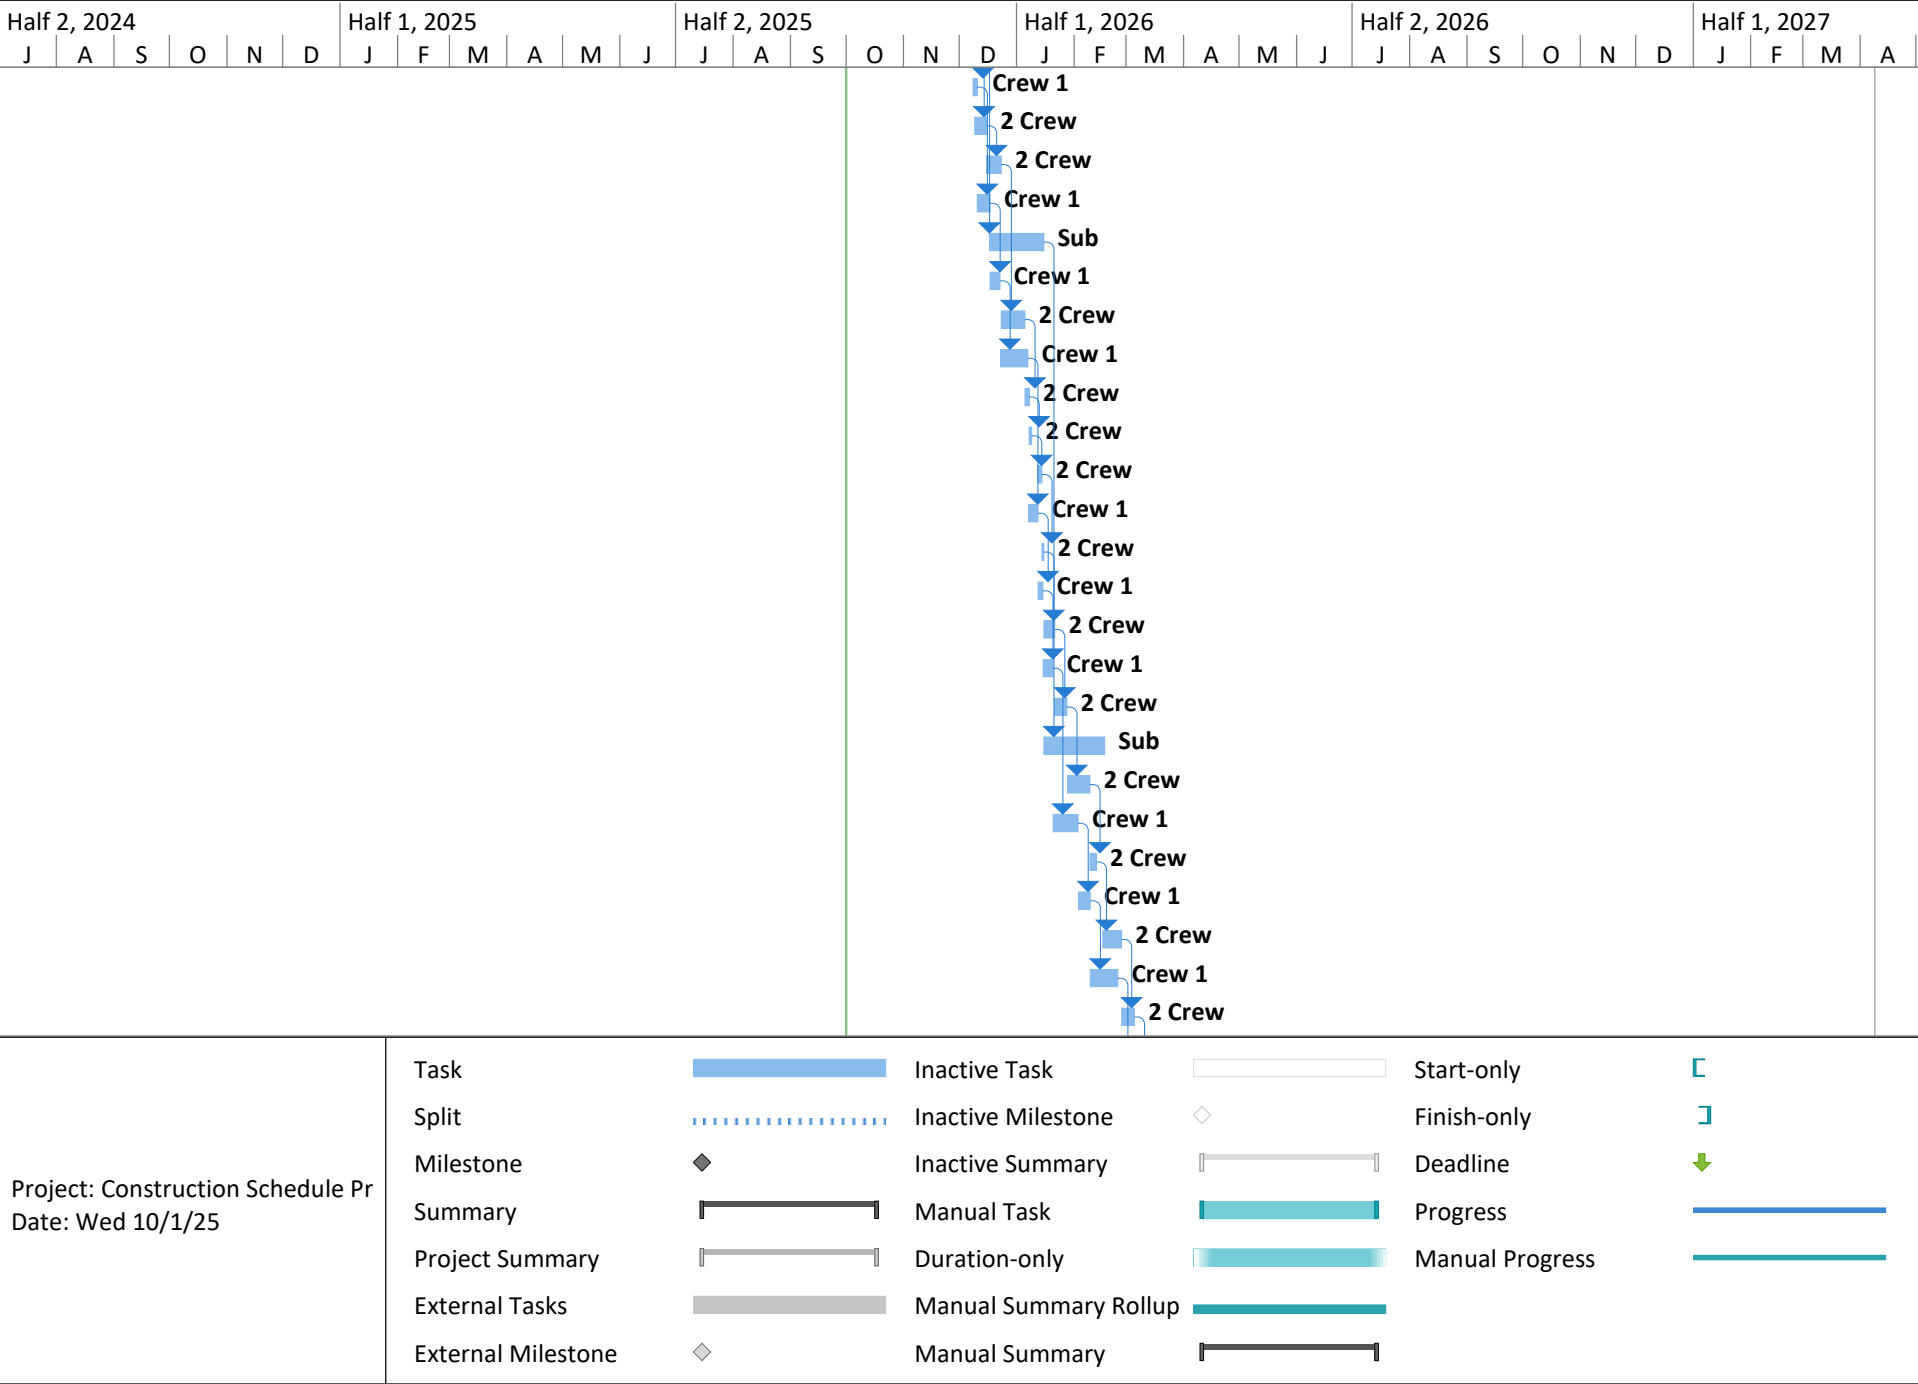


Project: Construction Schedule Pr
Date: Wed 10/1/25

SUBJECT TO CHANGE

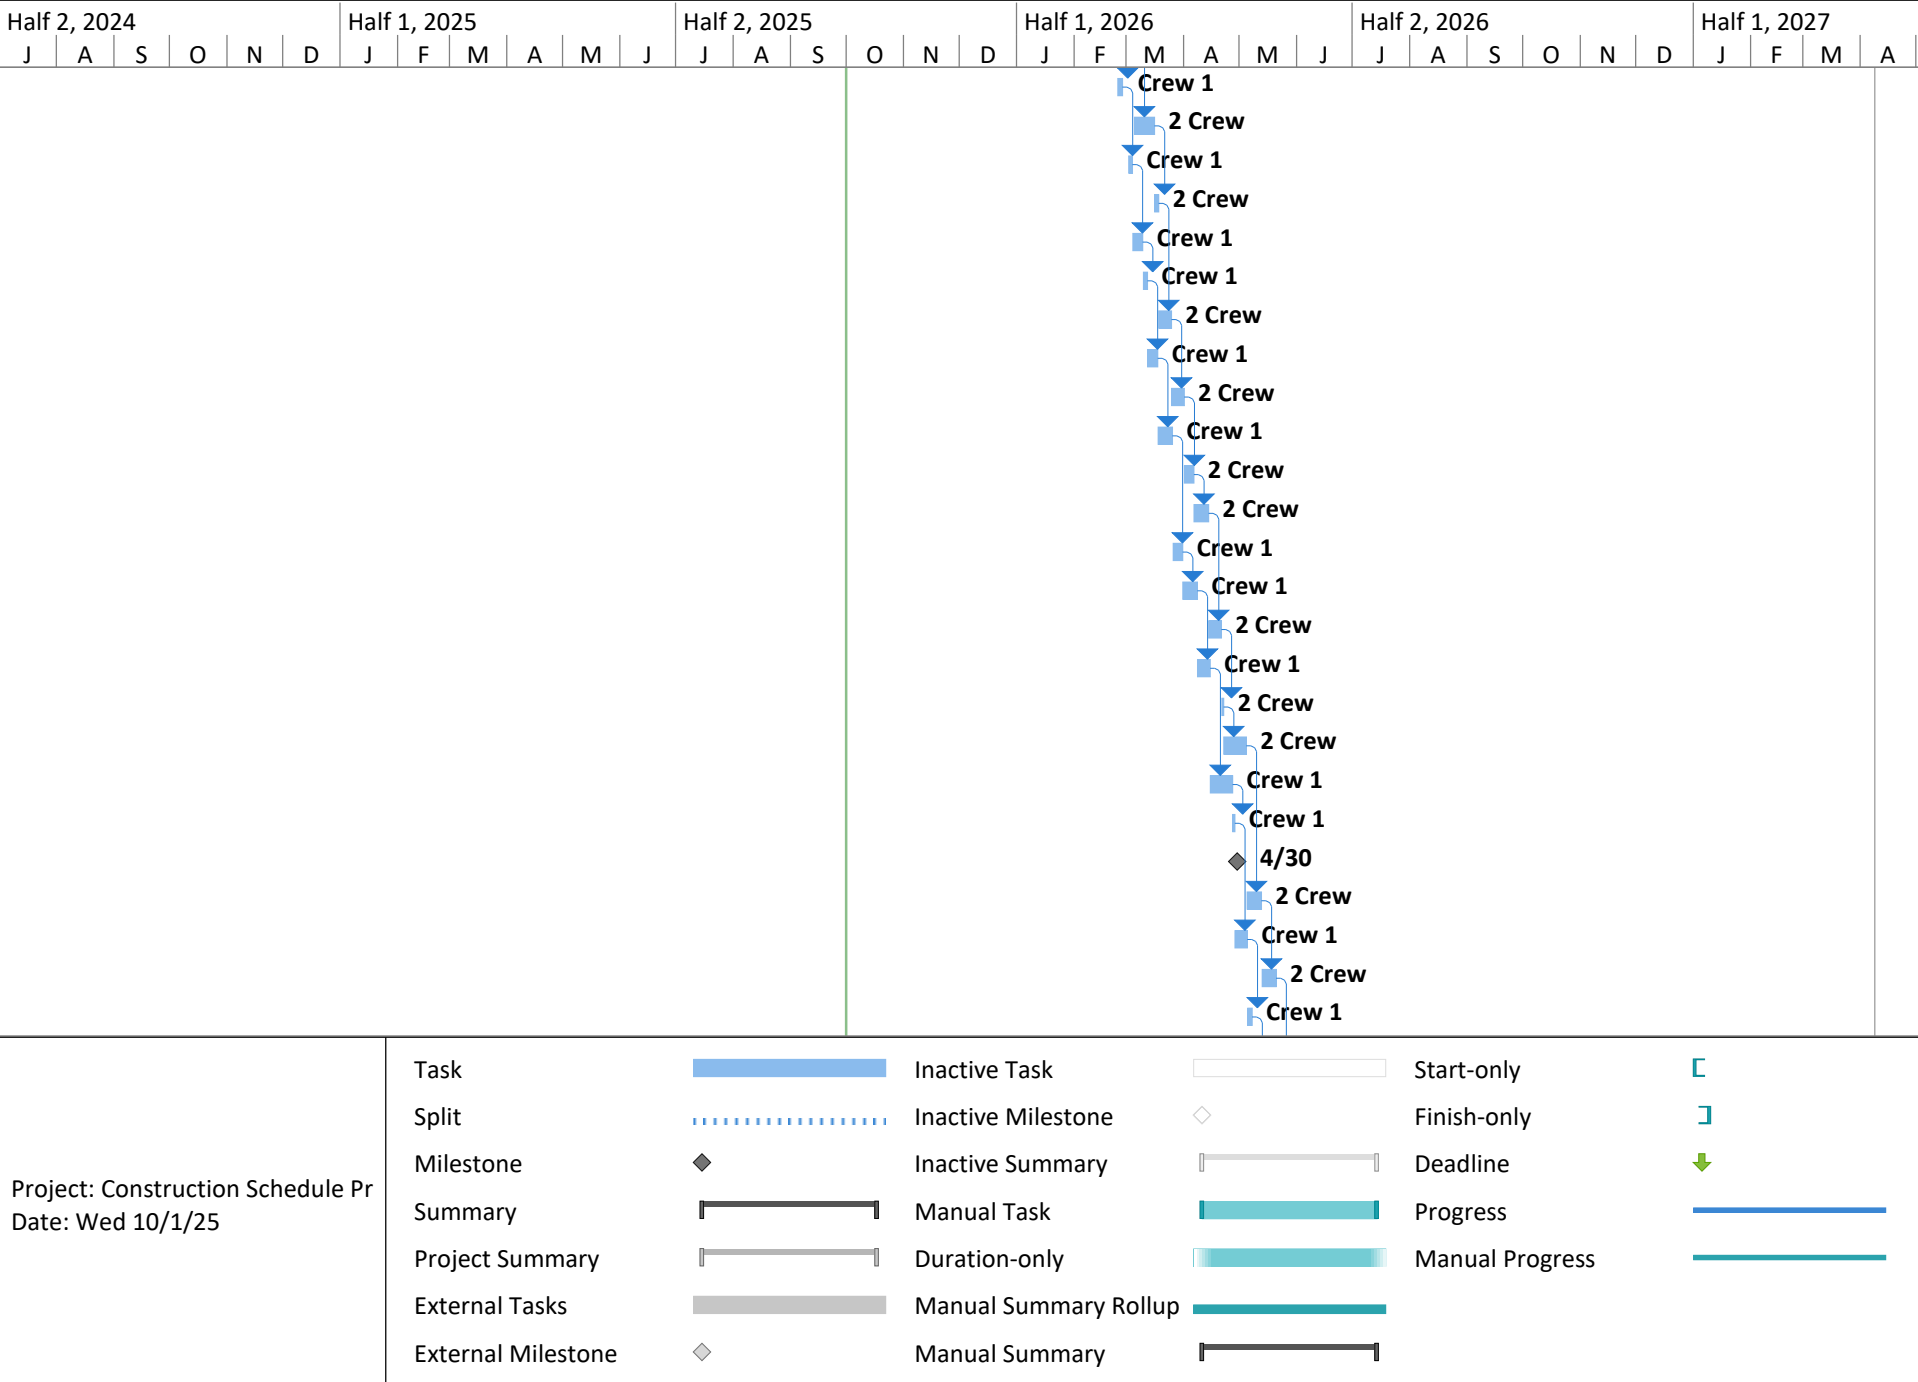


Project: Construction Schedule Pr
Date: Wed 10/1/25

SUBJECT TO CHANGE

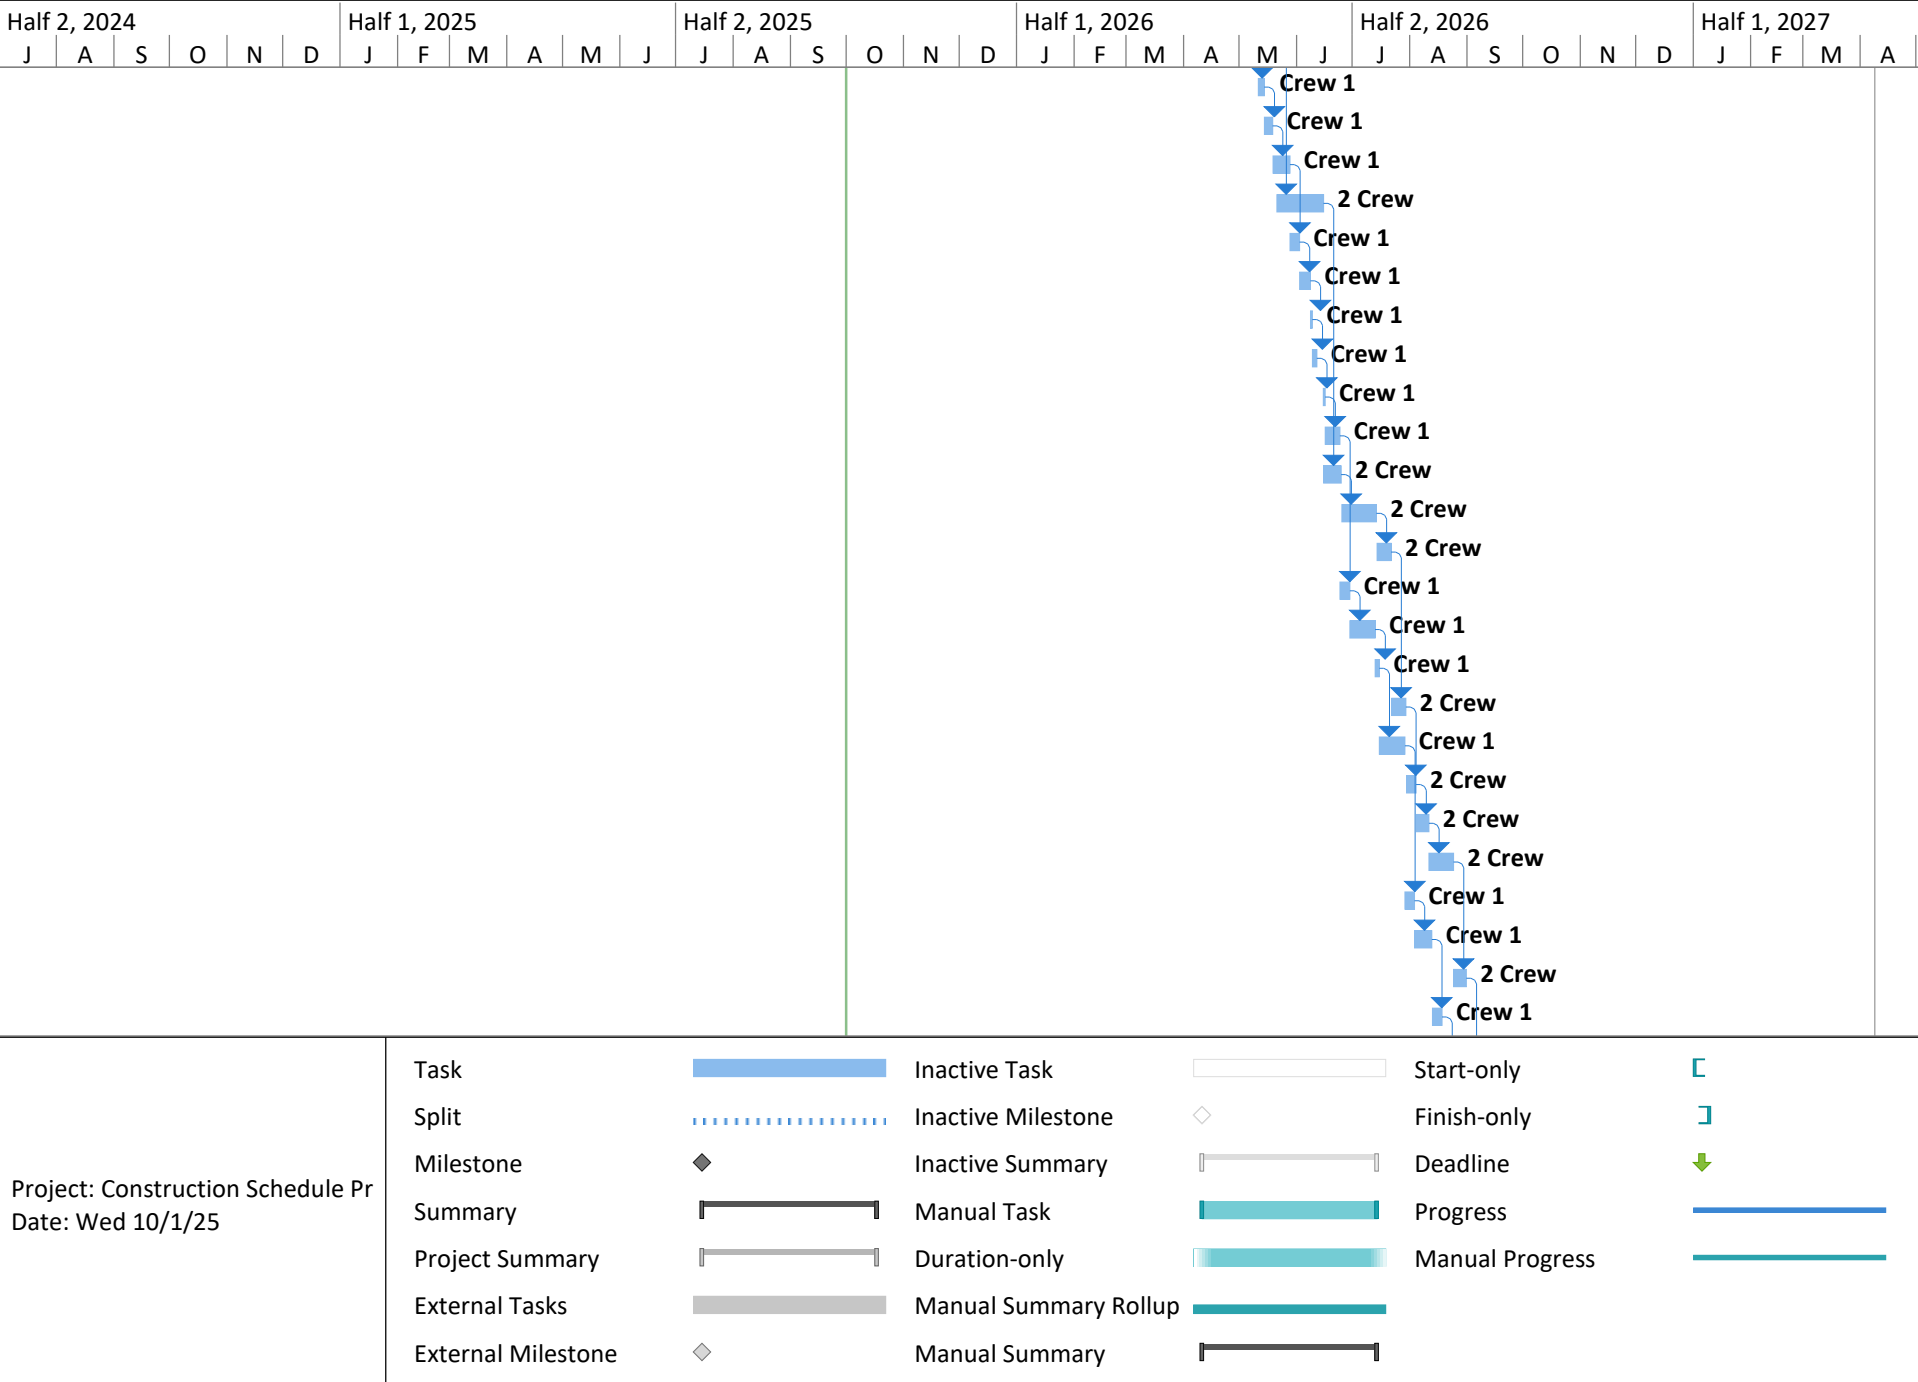

SUBJECT TO CHANGE

[illegible]

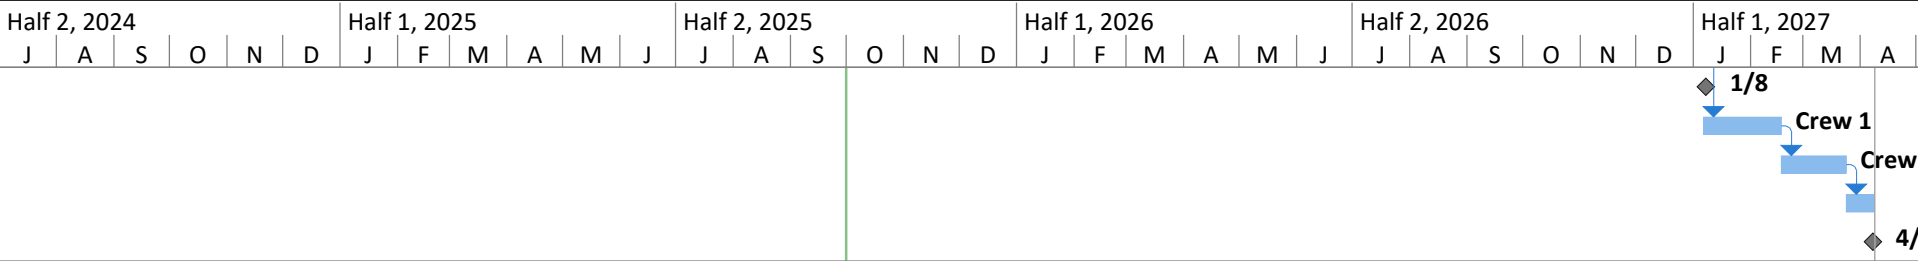

Project: Construction Schedule Pr Date: Wed 10/1/25	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Progress	
	Project Summary		Duration-only		Manual Progress	
	External Tasks		Manual Summary Rollup			
	External Milestone		Manual Summary			

SUBJECT TO CHANGE
